



Driving Global Consistency in Capital Project Delivery

Ricky Kyle
Karl Hall



Turner & Townsend

Introductions



Ricky Kyle
Director



Karl Hall
Associate Director



Turner & Townsend

“Our major project expertise, combined with proven frameworks and trusted partners, enables us to drive global consistency in capital project delivery. By leveraging best-in-class project and programme experience, we accelerate transformation at pace, underpinned by our robust and proven methodologies to ensure lasting value”

Ricky Kyle
Director



The Ask

A global Life Sciences client came to us asking for a planning solution that could be embedded globally, with consistency, and within a live environment



Implement a Unified Planning System

Establish and embed a globally integrated planning platform to streamline capital project management, enhance collaboration, and ensure alignment across all regions and functions



Standardised Global Planning Methodology

Develop and adopt a consistent, scalable approach to capital planning across the global portfolio, enabling transparency, comparability, and strategic prioritization of investments



Performance transparency

Create a single source of the truth for capital data to support accurate, real-time reporting and generate actionable insights that drive informed decision making

Driving Global Consistency



Hosting, Migration &
Configuration




Driving Behavioral and
Cultural Change



Process Enhancement
(Our Cube Methodology)



Performance Transparency



Protecting Delivery

Enterprise Planning Solution



Hosting, Migration & Configuration

Partnering with RPC to deliver an enterprise planning solution within a major global life sciences environment – enabling scalability, resilience, and performance for future growth



Turner & Townsend

Achieved exponential growth - Performance & server issues experienced with the previous hosting partner.

Growth-driven challenges - The scale and pace of expansion began to outgrow our previous hosting setup, impacting performance and reliability.

Strategic partnership with RPC - To support continued growth and ensure reliability, we engaged RPC as our hosting partner.

Embedding the foundation to achieve the ask:



Commercial Appraisal




**Requirements Management
& Scope Definition**



**Developed Migration
Plan**



**Creation of 8 Databases &
assigning of 100+ Users**



**Development of Database
Structures to mirror previous
hosting platform**



**Testing efficiency &
performance before
Live Migration**



Driving Behavioral & Cultural Change

Beyond systems and processes, it is culture and behavior that determine lasting success. By shaping mindsets, building trust, and embedding the right behaviors, we enable meaningful change and create the foundation for consistent, long-term results.



Utilisation of various planning software (MSP, Excel, PPT)



Outdated PCON Governance Framework



Prioritisation of Cost over Schedule



Inconsistent ways of working cross site



Lack of Training




Unclear Reporting Lines



Process Enhancement

The winning formula is our Cube methodology, offering a tailored global delivery framework that drives impactful, purpose-built control and sustained performance.

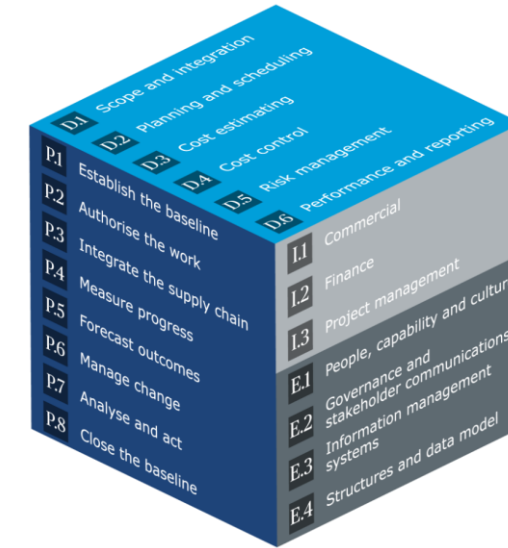

Our Schedule management team, utilise our Cube toolkit, with access to our proven:

Quick guides & procedures

Quick Guide to the Planning and Scheduling Discipline
C&P-D2-GN-xxx

Quick Guide to Schedule Hierarchy, Level, Class and Type
C&P-D2-GN-xxx

Quick Guide to Basis of Schedule, Benchmarking and Schedule Assurance
C&P-D2-GN-xxx

Quick Guide to Integrated Activity Planning and Rolling Wave Planning
C&P-D2-GN-xxx

Tools and templates

Planning & Scheduling Discipline Work Instruction
C&P-D2-WI-001

Basis of Schedule Template
C&P-D2-TE-002

Schedule Assurance Toolkit
C&P-D2-TE-004

Milestone Register Template
C&P-D2-TE-006

Schedule Template
C&P-D2-TE-001

Schedule Management Plan
C&P-D2-TE-003

Schedule Estimate and Productivity Worksheet
C&P-D2-TE-005

Milestone Definition Sheet Template
C&P-D2-TE-007

Schedule Quality Checklist
C&P-D2-TE-011

Critical Path Analysis and Management Guidance
C&P-D2-GN-002

Resource Analysis Histograms Template
C&P-D2-TE-009

SC&P-D2-TE-011schedule Benchmark Report Template
C&P-D2-TE-008



Performance Transparency

By unlocking global schedule transparency through Primavera, we've shifted from assumptions to assurance, empowering teams with data-driven insights that drive accountability, alignment, and smarter decisions.





Protecting Delivery

Utilising the insights from impactful reporting, we have worked with this client to stop risks becoming issues and ultimately protect their investment



Global consistency, local delivery

19+ Sites
3 Continents
7+ Time Zones



Site delivery partner

stepping into delivery locally while embedding global consistency



Major project interventions

protecting delivery through transparency and targeted interventions



EVM training

for effective adoption, management and accuracy

61

Countries

245

Offices

22,731

People

112

Nationalities

11,627

Projects
